REPROCESSING

LINE DR-3021-77 2400% S.P. 1 S.P. 376

DEPHASING-FREQ.DECON
T.V.F.

Agip S.p.A.
Attività Minerarie – REIT

| ALL. | DATA | DIS. N. |
|---|---|---|
| 3B | MARZO '81 | 206/3 |

AREA ITALY ZONE D

PROSPECT MAR IONIO

| RECORDING | DATA | PLAYBACK | DATA |
|---|---|---|---|
| CONTRACTOR | C.G.G. | DATUM PLANE | SEA LEVEL |
| SHIP | VERSEAU | VERTICAL SCALE | 1 SEC.= 10 CM. |
| MAGNETIC RECORDER | SN 338 | HORIZONTAL SCALE | 1 KM.= 8 CM. |
| SAMPLE RATE | 2 MS. | PREPROCESSING REEL | 8147 |
| RECORD LENGTH | 4000 MS. | STACK REEL | 8993 |
| FILTER L.C. | 12,5 HZ. | PREVIOUS PROCESSING | FEBRUARY, 1978 |
| ALIASING FILTER | 125 HZ. | DATE | JULY, 1980 |
| DATE | NOVEMBER, 1977 | | |
| SPREAD CONFIGURATION | 157-1332 M. | | |
| TRACE / S.P. | 48 | | |
| GROUP / INTERVAL | 25 M. | | |
| GEOPHONES / GROUP | 24 | | |
| GEOPHONES / HZ | HC-201 9HZ. | | |
| ENERGY SOURCE | VAPORCHOC | | |
| DEPTH | 2,5 TO 4 M. | | |

SP 1 48
157 1175

PROCESSING

EDIT F.P.(GEOPHONE AMPLITUDE)
DEBUBBLE
PREPROCESSOR CDP GATHER
SURFACE SYSTEM DEPHASING
FREQ. DECON (OPERATOR 400 MS.)
VELOCITY ANALYSIS ▼
NMO CORRECTIONS
2400 % STACK
FAN FILTER
TIME VARIANT FILTER

TVF PARAMETERS

| | | |
|---|---|---|
| UPPER ZONE | 10HZ 24DB | 80HZ 48DB |
| MIDDLE ZONE | 10HZ 24DB | 70HZ 48DB |
| LOWER ZONE | 10HZ 24DB | 45HZ 48DB |

POLARITY CONVENTION

COMPRESSIONAL WAVES - WHITE ON SECTION
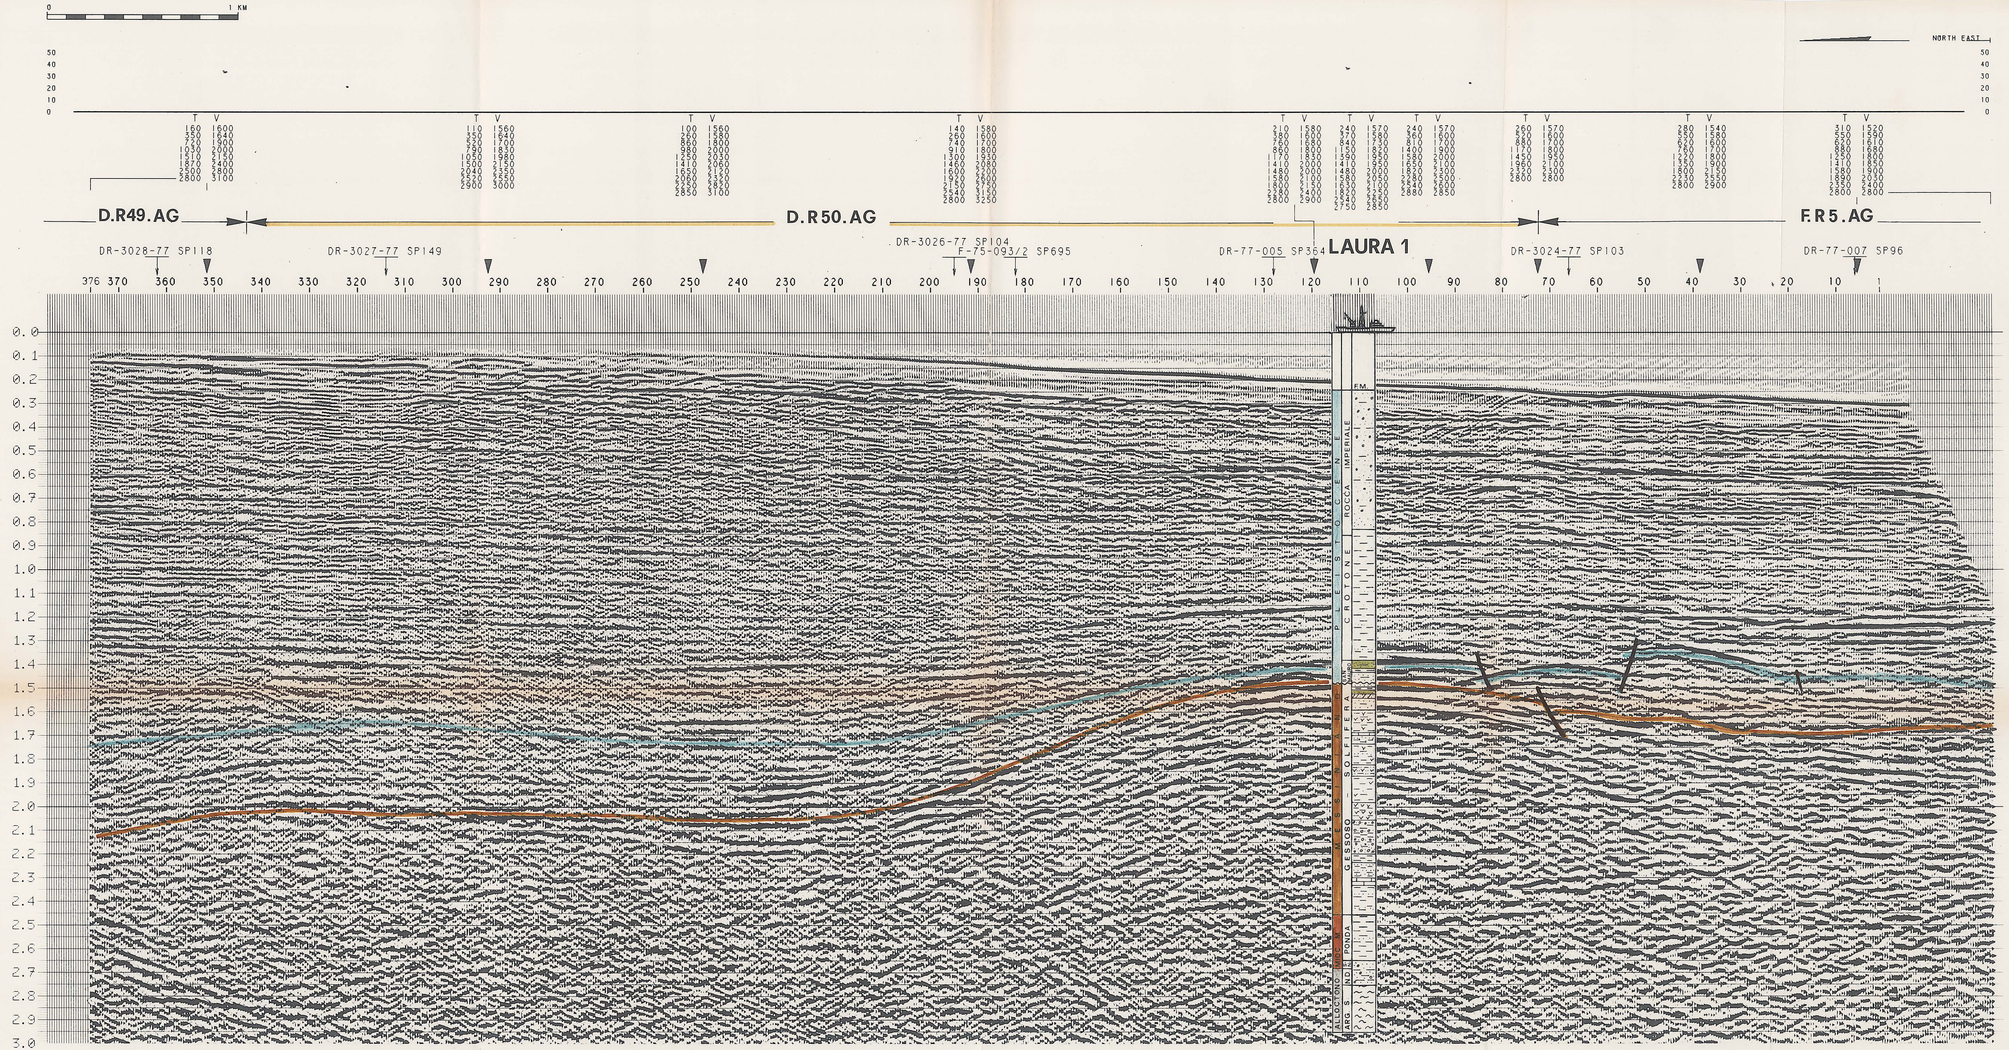
AZIONE IDROCARBURI
di NAPOLI
12 MAG. 1981
Prot. 1508
Sez. Posiz.
